SCHOOL BUILDING COMMITTEE MEETING AGENDA

Meeting Date: March 21, 2024

Meeting Time: 4:00 PM

Project Name: Tri-County Regional Vocational Technical High School

Project Number: MP20-28

Meeting Purpose: SBC Meeting No. 036

Location: Tri-County Regional Vocational Technical High School – Library

Address: 147 Pond Street, Franklin, MA 02038

Prepared By: E. Grijalva

- 1. Call to Order & Intro
- 2. Previous Topics & Approval of February 15, 2024, Meeting Minutes
- 3. Invoices and Commitments for approval
 - > DWMP February Invoice, in the amount of \$100,000.00
 - DRA February Invoice, in the amount of \$975,000.00
 - DRA February Professional Services Invoice, in the amount of -\$8,112.50
 - Consigli February Invoice, in the amount of \$31,191.00
 - > Rubin and Rudman LLP Invoice, in the amount of \$236.16
 - > Bullseye underground utility invoice, in the amount of \$450.00
 - Consigli: Sub soil exploration cost not to exceed 50K
- 4. DRA Update
- 5. Consigli Update
- 6. Solar Panel Array Update
- 7. Conservation Commission Update
- 8. Other Topics not Reasonably Anticipated 48 hours prior to the Meeting
- 9. Public Comment
- 10. Next Meetings
- 11. Adjourn



SCHOOL BUILDING COMMITTEE **MEETING MINUTES**



Project: Tri-County Regional Vocational Technical HS Subject:

School Building Committee Meeting No. 34

Location: ZOOM

Distribution: Attendees, Project File MSBA Module: 6- Detailed Design

Prepared By:

Project No:

Time:

Meeting Date:

4:00 PM E. Grijalva

MP20-28

02/15/24

Present

Brian Mushnick* SBC Chair

Karen Maguire* Superintendent Dan Haynes* Business Admin. Jonathon Dowse* SBC Member Harry Takesian* **Facilities Director** Michael Procaccini* SBC Member Brendan Bowen* SBC Member Bob Foley* Adult Ed. Dir

Dana Walsh SBC Member -TCRVTHS Principal

Trip Elmore DWMP- Project Director Mike Cox DWMP - Project Manager Elias Grijalva DWMP- Assistant PM DWMP- Assistant PM Rachel Rincon Vladimir Lyubetsky **DRA- Project Manager** Carl Franceschi DRA - Principal in Charge

Wayne Mattison G & V (Mechanical) **Bob Bravo** G & V (Electrical)

S. Johnson Consigli- Sr. Project Manager Kristy Lyons Consigli - Sr Pre-Con Manager

^{*}SBC Voting Member

Project: Tri-County Regional Vocational Technical High School Meeting: School Building Committee Meeting No. 35 – 02/15/2024

Page: 2

Item/ No.	Description	Action
35.1	Call to order : 4:09 PM meeting was called to order by SBC Chair B. Mushnick, 9 of 11 voting members in attendance.	Record
35.2	Previous Topics & Approval of January 18,2024 Meeting Minutes: A motion to approve the January 18,2024 previous meeting minutes as submitted was made by J. Dowse and seconded by B. Foley.	Record
	Discussion: None; Roll Call Vote: B. Foley (Y), B. Bowen (Y), D. Walsh (Y), M. Procaccini (Y), K. Maguire (Y), H. Takesian (Y), J. Dowse(Y), B. Mushnick (Y); Abstentions: None. All in favor. Motion passes.	
35.3	Invoices and Commitments for approval:	Record
	Invoice 1 : DWMP January Invoice, in the amount of \$100,000.00 A motion was made by M. Procaccini and seconded by J. Dowse for the approval of the DWMP January invoice.	
	Discussion: B. Foley shares his concerns about ensuring that the payment reflects the actual progress made by the Team. He suggests a need to form a verification mechanism, for example a schedule of values.	
	T. Elmore explains that this budgeting process involves setting up different funding categories for various stages of the project. We are currently in the construction documents phase, and the invoices reflect this stage. You're making periodic monthly payments, as we go through each of these phases.	
	B. Foley comments that there is a level of uncomfortableness for me in approving these large invoices without being able to compare them to a schedule of values.	
	C. Franceschi acknowledges B. Foley's concerns about the oversight and suggests establishing a requisition subcommittee to review the architect's work and ensure progress is on track.	
	Requisition Subcommittee Members: B. Bowen, Bob Foley, Karen Maguire, Dan Haynes, Trip Elmore, Vladimir, Carl Franceschi	
	Roll Call Vote : B. Foley (Y), B. Bowen (Y), D. Walsh (Y), M. Procaccini (Y), K. Maguire (Y), H. Takesian (Y), J. Dowse(Y), D. Haynes (Y), B. Mushnick (Y); Abstentions: None. All in favor. Motion passes.	

Project: Tri-County Regional Vocational Technical High School Meeting: School Building Committee Meeting No. 35 – 02/15/2024

Page: 3

Pā	gge: 3	
	Invoice 2: DRA January Invoice, in the amount of \$976,955.00	
	A motion was made by B. Foley and seconded by J. Dowse for the approval of the DRA January invoice. Discussion: None; Roll Call Vote: B. Foley (Y), B. Bowen (Y), D. Walsh (Y), M. Procaccini (Y), K. Maguire (Y), H. Takesian (Y), J. Dowse(Y), D. Haynes (Y), B. Mushnick (Y); Abstentions: None; All in favor. Motion passes.	
	Invoice 3 : DRA January Professional Services Invoice, in the amount of \$33,672.10	
	The motion was made by B. Foley and seconded by J. Dowse for the approval of DRA January Professional Invoice.	
	Discussion: V. Lyubetsky explains this invoice is related to Amendment No.006 Geotechnical related work.	
	Roll Call Vote: B. Foley (Y), B. Bowen (Y), D. Walsh (Y), M. Procaccini (Y), K. Maguire (Y), H. Takesian (Y), J. Dowse(Y), D. Haynes (Y), B. Mushnick (Y); Abstentions: None. All in favor. Motion passes.	
	Invoice 4: Consigli January Invoice, in the amount of \$31,191.00	
	The motion was made by J. Dowse and seconded by B. Foley for the approval of the Consigli January Invoice.	
	Discussion: T. Elmore explains this is for their preconstruction fee that is invoiced consistently every month.	
	Roll Call Vote : B. Foley (Y), B. Bowen (Y), D. Walsh (Y), M. Procaccini (Y), K. Maguire (Y), H. Takesian (Y), J. Dowse(Y), D. Haynes (Y), B. Mushnick (Y); Abstentions: None. All in favor. Motion passes.	
35.4	DRA Update: Mechanical and Electrical Systems	Record
	V.Lyubetsky introduces his two engineers in the meeting today, Wayne Mattison & Robert Bravo from G & V.	
	W. Mattison provides a HVAC progress update from schematic design to design development phase.	
	 Lifecycle Cost Analysis (LCCA) for HVAC Systems Compare various HVAC systems for vocational schools. Air Source Heat Pump, Water Source Heat Pump, VAV systems Compares installation costs versus the energy consumed, cost of maintenance replacement cost and operational costs. 	

Meeting: School Building Committee Meeting No. 35 – 02/15/2024

Page: 4

Variable Refrigerant Flow System (VRF) - Current Design

- Meets ASHRAE Standard 54: thermal comfort design & 62- ventilation standard.
- Meets international energy conservation code.
- Meets ASHRAE 90.1- Energy Standard for Building
- Meets NC & ANSI sound standards.
- Classrooms, Office, Conference rooms types of spaces
- System consists of:
 - o Roof or Ground Mounted Heat Pumps
 - Ceiling Cassettes
 - Concealed Fan coil Units
 - o Refrigeration Piping w/ Branch Controllers
 - Energy Recovery Units for Ventilation
- System Provides:
 - Simultaneous Heating & Cooling
 - o Individuals Space Temperature Control
 - o Built-in Redundancy through the use of multiple compressors
- · Gymnasium, Auditorium & Student Dining
 - o served by split type air heat pumps.
- Classrooms
 - Heating & Cooling handled by VRF System.
 - o Ventilation provided by roof mounted packaged air source heat package.
 - Teachers can control their own environment.
- Roof
- o Air source heat pumps that provide ventilation

Discussion:

- B. Bowen asks if these rooms have a fan coil system or a quiet system.
- W. Mattison replies, the ceiling cassettes are a ductless fan coil, extremely quiet, meets LEED standard for enhanced acoustical environment.
- B. Bowen asks if the ceiling cassettes paired with any specific ratings within the room or ceiling type?
- V. Lyubetsky replies that as part of the LEED submission, our acoustic engineers Acentech are going to provide the reverberation time calculations.
- W. Mattison states Acentech will review our design; we provide them with our equipment selections and they will make recommendations. It's an iterative process.

^{*}The whole system is controlled by a building management system, a central computer, where all the scheduling of the equipment exists.

Meeting: School Building Committee

Meeting No. 35 - 02/15/2024

Page: 5

B. Bowen asks are there any potential issues arising from activities within the shop that could affect the performance or effectiveness of the energy recovery system.

W. Mattison replies, in various shops like the woodshop, automative, welding plumbing and HVAC, industrial equipment such as wood dust collectors, vehicle exhaust systems, and welding fume capture equipment is utilized to manage emissions. These shops also use MERV 8 filters on the return side of the energy recovery system's wheel to capture airborne dust particles. Additionally, MERV 13 filters are employed to further enhance indoor air quality, aligning with the best engineering practices, though it's not mandated. This comprehensive filtration system helps protect the wheel from contamination, minimizing the need for extensive cleaning.

K. Maguire asks, is this system adequate given the complexities of vocational program spaces and the challenges with air circulation and ventilation, particularly considering colleagues experiences with system issues in other schools, to ensure we're selecting the most appreciate solution for our needs.

W. Mattison states our systems are designed in accordance with the Industrial Hygienist handbook, which follows OSHA standards, ensuring that vocational school environments meet industrial safety requirements akin to those of professional automotive shops. These systems encompass extensive ductwork to capture emissions from various equipment such as table saws and belt sanders in the woodshop and soldering stations in the HVAC shop, with dedicated exhaust systems for areas like nail benches in Cosmetology to address specific chemical hazards. Despite being overlooked as industrial environments, vocational schools require meticulous ventilation planning to ensure the safety and well-being of students and staff.

- B. Mushnick asks what is the expectancy of the filters?
- W. Mattison replies, MERV 13 about a year and MERV 8 about 2 years to replace.
- H. Takesian comments, that is what we are currently doing now for current filters in place.

R. Bravo provides an Electrical progress update from schematic design to design development phase.

- Trilogy services to the building with two electric utility company transformers on-site.
- Two switchboards inside the building are estimated at 4000 amps at 277/480 volts each.
- Panel boards and transformers were distributed throughout the building.
- Individual panel boards for each shop equipped with shunt trip breakers and emergency power-off buttons.
- Planning for an 800-kW diesel generator housed in a soundproof enclosure.
- Adjustments made from originally planning two generators to one, requiring reassessment of emergency power equipment.

Meeting: School Building Committee Meeting No. 35 – 02/15/2024

Page: 6

- Implementation of an addressable fire alarm system with voice evacuation, typically specifying an auto call system for public bids.
- Lighting Fixtures LED
- Exterior lighting fixtures include site and wall-mounted fixtures, with lighting controls featuring occupancy sensors with dimmers and daylight harvesting in each room.
- Exterior lighting controlled by relay panels with occupancy sensors adjusting light intensity based on motion detection, integrating with on-site cameras for enhanced security.
- Compliance with energy code requiring automatic receptacle control, with 50% of receptacles in specific rooms controlled by occupancy sensors.
- Implementation of a bi-directional amplifier system to amplify police and fire radios as required by code.
- Provision of electric vehicle charging stations, typically constituting 2% of overall spaces to meet green vehicles credit in LEED certification.
- Installation of a mass notification system including amber strobes for active shooter alerts, with control points for communication.
- Implementation of a lightning protection system for the building.

Discussion:

D. Walsh asks should we involve the Franklin Fire Department in our discussions regarding the active shooter systems.

V. Lyubetsky comments that we plan on meeting with the fire department to review the system and receive their feedback.

35.5 **Solar PV Array Update**

Record

- D. Haynes provides an update.
- Contacted Solect Energy to provide a cost to remove the solar panels.
- Option 1: exit the contract with luminance, take ownership of the panels and have them removed.
- Option2: Clause in contract: substitution of premises, which would be the new building to redevelop the solar, but we're responsible for the cost of relocating the system.
 - Question: What is the scope of work for this depth. If they remove the panels, they remove the structures that hold the panels, but about what about the underground conduit.
 - o Question: When could they commence solar work on the new building?
 - 80% would be on the rooftop; the rest will be top of bleachers/ parking canopy.

Discussion:

Project: Tri-County Regional Vocational Technical High School Meeting: School Building Committee Meeting No. 35 – 02/15/2024

Page: 7

	 School Building Committee Meeting School Building Committee In-person Meeting – March 21, 2024; Location: Tri-County Regional Technical High School 	
35.8	Next Meeting:	Record
35.7	Public Comment: Discussion: None	Record
	 Discussion: J. Dowse request an update on environmental issues in the solar fields? B. Mushnick provides an update: Standstill with the town regarding differing perspectives on the presence of wetlands on the property Retained an environmental lawyer Glenn A. Wood to present our side of the discussion to the town. Further updates will be provided. 	
35.6	 T. Elmore comments that the scope of work would be anything that sits on the surface and anything that sits underground can be removed by Consigli. It will be more cost effective. T. Elmore comments the summer, before the students go back to school, would be a good time to commence solar panel work on the new building. S. Johnson suggest starting the process sooner then later, due to the number of applications. B. Bowen asks is the scope of the removal defined. Or should this be part of the scope question? D. Haynes replies, Solect puts the panels on a train to Georgia to get recycled, which will be part of the cost projections. B. Mushnick comments that in the state of Massachusetts you can just dispose of them. It's not a hazardous material. Ultimately, we'd love to recycle and have someone else reuse them. It's trying to find someone willing to take them and pay. Other Topics not Reasonably anticipated 48 hours prior to the Meeting. 	Record
	T. Elmore asks S. Johnson if it is possible to leave the screw anchors in place and address their removal through civil?S. Johnson replies, we do not need the solar removal company to do that portion of the work.	

Meeting: School Building Committee

Meeting No. 35 - 02/15/2024

Page: 8

	School Building Committee Meeting – April 25, 2024; Location: TBD	
	Discussion: None	
35.9	Adjourn: 5:37 PM motion was made by K. Maguire and seconded by J. Dowse to adjourn the meeting.	Record
	Discussion: Roll Call Vote: B. Foley (Y), B. Bowen (Y), D. Walsh (Y), M. Procaccini (Y), K. Maguire (Y), H. Takesian (Y), J. Dowse(Y), D. Haynes (Y), B. Mushnick (Y); Abstentions : None; All in favor. Motion passes.	

Sincerely,

DORE + WHITTIER

Elias Grijalva

Assistant Project Manager

Cc: Attendees, File

The above is my summation of our meeting. If you have any additions and/or corrections, please contact me for incorporation into these minutes.

March 21, 2024



Project Name: Tri-County

Subject: Budget Update

1. Invoice(s): recommended for payment

Vendor	Invoice	Amount
Dore + Whittier	25	\$100,000.00
DRA	23	\$975,000.00
DRA	PSS6-2	(\$8,112.50)
CCC	3	\$31,191.00
Rubin & Rodman	1176543	\$236.16
Bullseye	201655	\$450.00

\$1,098,765

2. New Commitment(s):

Vendor	Amendment No. Amount			
CCC	1	NTE - \$50,000		

3. Budget Revision Request(s): -

4. MSBA Reimbursement Status:

PR No.	Payment Request Date	Submitted Amount	Ineligible Project Costs	Eligible Project Costs	Eligible Grant	Recommended Payment Amount	MSBA Last Payment Date	MSBA Payment Amount
1	12/6/2023	\$10,000	\$0	\$10,000	\$5,289	\$0	1/28/2022	\$5,289
2	2/17/2022	\$20,000	\$0	\$20,000	\$10,578	\$0	3/31/2022	\$10,578
3	4/8/2022	\$39,250	\$0	\$39,250	\$20,759	\$0	5/19/2022	\$20,759
4	6/23/2022	\$102,000	\$0	\$102,000	\$53,948	\$0	7/28/2022	\$53,948
5	8/1/2022	\$49,880	\$0	\$49,880	\$26,382	\$0	9/9/2022	\$26,382
6	10/26/2022	\$67,750	\$0	\$67,750	\$35,833	\$0	12/15/2022	\$35,833
7	12/20/2022	\$98,886	\$0	\$98,886	\$52,301	\$0	2/2/2023	\$52,300
8	3/10/2022	\$117,740	\$0	\$117,740	\$62,273	\$0	4/6/2023	\$62,273
9	5/16/2023	\$145,750	\$0	\$145,750	\$77,087	\$0	6/23/2023	\$77,087
10	8/14/2023	\$311,790	\$0	\$311,790	\$164,906	\$0	9/8/2023	\$158,006
11	12/14/2023	\$34,695	\$0	\$34,695	\$54,967	\$61,867		\$0
12	2/14/2024	\$1,575,000	\$0	\$1,575,000	\$890,820	\$952,687		\$0
Total		\$2,572,741	\$0	\$2,572,741	\$1,455,143			\$502,455

Dore and Whittier Management Partners, LLC

Please send payments to; 212 Battery Street Suite 1 Burlington, VT 05401

Tri-County Regional Technical School District

147 Pond Street Franklin, MA 02038 Invoice number 00025

Date 02/27/2024

Project 21-0122 TRI-COUNTY REGIONAL TECHNICAL HIGH SCHOOL

Description		Contract Amount	Prior Billed	Current Billed	Remaining	Total Billed
Pre Designer Selection		40,000.00	40,000.00	0.00	0.00	40,000.00
Feasibility Phase		130,000.00	130,000.00	0.00	0.00	130,000.00
Schematic Design		105,000.00	105,000.00	0.00	0.00	105,000.00
Construction Documents		1,900,000.00	400,000.00	100,000.00	1,400,000.00	500,000.00
Bidding		200,000.00	0.00	0.00	200,000.00	0.00
Construction Administration		4,700,000.00	0.00	0.00	4,700,000.00	0.00
Closeout		200,000.00	0.00	0.00	200,000.00	0.00
	Total	7,275,000.00	675,000.00	100,000.00	6,500,000.00	775,000.00

Invoice total

100,000.00

Aging Summary

Invoice Number	Invoice Date	Outstanding	Current	Over 30	Over 60	Over 90	Over 120
00024	01/30/2024	100,000.00	100,000.00				
00025	02/27/2024	100,000.00	100,000.00				
	Total	200 000 00	200 000 00	0.00	0.00	0.00	0.00



Invoice

Karen Maguire Superintendent Tri-County Regional Vocational Technical School Di 147 Pond Street Franklin, MA 02038

Project-Tri-County Regional Vocational Technical

February 29, 2024 Project No: 22001.00 Invoice No: 0000023

Percent

Total this Invoice

Professional Services from February 1, 2024 to February 29, 2024 Fee

Billing Phase	Fee	Complete	Earned	
Feasibility Study	285,000.00	100.00	285,000.00	
Schematic Design	340,000.00	100.00	340,000.00	
Design Development	7,500,000.00	43.00	3,225,000.00	
Construction Documents	9,550,000.00	0.00	0.00	
Bidding	150,000.00	0.00	0.00	
Construction	3,800,000.00	0.00	0.00	
Completion	150,000.00	0.00	0.00	
Total Fee	21,775,000.00		3,850,000.00	
		evious Fee ing	2,875,000.00	
	Cu Bill	rrent Fee ing	975,000.00	
	Total Fee			975,000.00

If you have any questions regarding this invoice, please contact Judy Gill at 617-964-1700 or e-mail gill@ draws.com.

cc:telmore@doreandwhittier.com

\$975,000.00



High-level summary of the progress for the activities during the Design Development (DD) Phase of the Proiect:

- Constructability and Construction Phasing review with the Project Team –weekly meetings, ongoing.
- Geotechnical Investigation completed, report issued by OTO. Further additional investigation within the existing solar panel area is being discussed with the Project Team.
- Hazardous Material Investigation work in progress, preliminary report and cost estimate issued by OTO for the DD Cost Estimate.
- Background sound study completed, existing conditions measurements and report.
- Existing site water pressure investigation / study completed, report issued to the cost estimators for pricing.
- Building Code analysis and report completed (further minor updates will be provided as the project design progress)
- Design Team coordination meetings weekly meetings, ongoing.
- DD Phase cost estimate set drawings Completed (Over 500 pages, issued to the estimators on schedule 3/18)
- DD Phase cost estimate set outline specifications Completed (issued to the estimators on schedule 3/18)
- MSBA Submission information work in progress
- Early Site Enabling Bid Package work in progress, weekly meetings with the Project Team
- Department Meeting –work in progress (equipment review and selection)
- Color / Design Meetings work in progress.
- Permitting ANRAD submitted, regular meetings with the Conservation Commission and the Project Team
- Permitting NOI submission expected before the end of March.
- Permitting Planning Board Site Plan Review submission expected Mid-April



Invoice

Karen Maguire Superintendent Tri-County Regional Vocational Technical School Di 147 Pond Street Franklin, MA 02038

February 29, 2024 Project No: 22001.06 Invoice No: 0000002

Project-Tri-County Regional Amendment 6 Geotech

Professional Services from February 1, 2024 to February 29, 2024

Consultants

O'Reilly, Talbot & Okun Associate	es, Inc. /Inv 55025 -Note 1				
O'Reilly, Talbot & Okun Associate	es, Inc. /Inv 55116-Note 2	- 1,000.00			
O'Reilly, Talbot & Okun Associate	es, Inc. /Inv 55147	5,625.00			
Total Consulta	ants	1.1 times	-7,375.00	-8,112.50	
Billing Limits	Current	Prior	To-Date		
Total Billings	-8,112.50	33,672.10	25,559.60		
Limit			123,200.00		
Remaining			97,640.40		
		Total this I	nvoice	-\$8,112.50	

Note 1) This was invoiced in January in error. These tasks are Preliminary Services and are DRA's responsibility.

Note 2) This was invoiced in January in error. This task of Design Phase Meetings is DRA's responsibility.

If you have any questions regarding this invoice, please contact Judy Gill at 617-964-1700 or e-mail gill@ draws.com.

cc:telmore@doreandwhittier.com



Consigli Construction Co., Inc. 72 Sumner Street Milford, MA 01757 (508)473-2580

Tri County Reg. Voc. Technical HS 147 Pond Street

Date:

Franklin, MA 02038

INVOICE ID: 3

DATE: February 29,2024

Period From: 2/2/2024 To: 2/29/2024

Item Id	Description	Contract Amount	Percent Complete	Total Billed	Previous Billed	Total This Invoice
22-000	Tri County Reg. Voc. Tech. HS					
22-001	PO 20231640					
22-100	Schematic Estimate Requirement	25,000.00	100.00 %	25,000.00	25,000.00	
22-200	Post-SD Precon Services	374,300.00	16.67 %	62,382.00	31,191.00	31,191.00
	Total	399,300.00	21.88 %	87,382.00	56,191.00	31,191.00
Contract Summary Original contract amount Approved changes Revised contract amount Invoiced to date Remaining to invoice Current Payment Due Percent billed Retainage balance		399,300.00 <u>0.00</u> 399,300.00 <u>87,382.00</u> 311,918.00 \$31,191.00 21.88 % 0.00				
Approved by	v.					
	•					
Name:						
Title:						



53 STATE STREET | BOSTON, MA 02109 | P:617-330-7000 500 UNICORN PARK DRIVE, SUITE 502 | WOBURN, MA 01801 | P:781-933-5505

Glenn A. Wood

Direct Dial: 617-330-7016

E-mail: GWood@rubinrudman.com

Return Address: Boston

March 7, 2024

By Email - maguire@tri-county.us and haynes@tri-county.us

Karen Maguire, Superintendent Dan Haynes, Business Manager Tri-County Regional Vocational Technical High School 147 Pond Street Franklin, MA 02038

RE:

147 Pond Street, Franklin, MA

Our File No.: 27408-1

Dear Karen and Dan:

Enclosed please find an invoice for our services rendered through February 26, 2024. We deducted the amount due out of your client funds account leaving a remaining balance now due.

If you wish to pay this invoice with an American Express, MasterCard or Visa card please see enclosed credit card authorization form.

If making payment by check, please make payable to "Rubin and Rudman LLP" and please provide your File Number or our Invoice Number for proper credit. Thank you for your attention to this invoice.

Sincerely yours,

Glenn A. Wood

Encl.



53 State Street Boston, MA 02109 *T* 617-330-7000 *F* 617-330-7550

Tri-County Regional Vocational Technical High School Karen Maguire 147 Pond Street Franklin, MA 02038

> Invoice Date: March 7, 2024 Invoice Number: 1176543

> > GAW

TOTAL AMOUNT DUE THIS INVOICE \$ 236.16

Client: 27408	Tri-County Regional Vocational Technical High School	
Matter: 001	147 Pond Street, Franklin, MA	
TOTAL FEES THIS INVOI	CE	5,181.00
TOTAL DISBURSEMENTS	S THIS INVOICE	55.16
TOTAL AMOUNT THIS I	NVOICE	\$ 5,236.16
Less Trust Applied		(5,000.00)
TOTAL AMOUNT DUE		\$ 236.16
	Please Use One of our Convenient Payment Options	
Payment via ACH:	Bank Name: Eastern Bank	
	ABA/Routing Number:	
	Account Number:	
Payment via Wire:	Bank Name: Eastern Bank	
(bank wire fees may apply)		
	SWIFT Code: EASRUS3B	
	Account Number:	
	Bank Address: 195 Market Street, Lynn MA 01901	
Payment via Check:	Rubin and Rudman LLP	
	53 State Street	
	15th Floor	
	Boston, MA 02109	
Tax ID:	04-2202844	



Invoice Date: March 7, 2024 Invoice Number: 1176543

GAW

Page 2

Client: 27408 Matter: 001 **Tri-County Regional Vocational Technical High School**

147 Pond Street, Franklin, MA

MONEY ON ACCOUNT

Trust Previous Balance (Eastern Bank IOLTA)

Trust Applied to this Invoice

Trust Balance (Eastern Bank IOLTA)

5,000.00 (5,000.00)

\$ 0.00



Invoice Date: March 7, 2024 Invoice Number: 1176543

> GAW Page 3

Client: 27408

Tri-County Regional Vocational Technical High School

Matter: 001 147 Pond Street, Franklin, MA

PROFESSIONAL SERVICES RENDERED:

DATE	TIMEKEEPER	Narrative		<u>Hours</u>
02/06/2024	GAW	Zoom meeting with project team and Con Comm CHARGE)	strategy. (NO	0.30
02/07/2024	GAW	Preparation of services letter to client. (NO CHAR	RGE)	0.50
02/08/2024	GAW	Finalization of services letter. Email corresponder same. (NO CHARGE)	nce with client on	0.50
02/13/2024	GAW	GAW Email correspondence with project team on weekly meetings.		0.30
02/15/2024	GAW	Teams meeting with project team.		0.40
02/16/2024	GAW	Email correspondence with B. Holmes on strategy correspondence with team on site visit scheduling		0.30
02/20/2024	GAW	Email correspondence with team on project statu correspondence with FCC Agent on same. Telepho B. Holmes on HCC ANRAD strategy. Review of Fra Bylaw/Regulations and WPA Regulations. Detailed site plans and FCC peer review.	one conference with nklin Wetlands	1.50
02/21/2024	GAW	Telephone conference with B. Hoyerman (x2) on visit. Email correspondence with FCC Agent on per Telephone conference with S. Powers on same. E with project team and client on ANRAD/NOI strat	nding ANRAD filing. mail correspondence	1.20
02/21/2024	TMF	Evaluate status of matter and position of Commis array detention basins; communications regarding		0.60
02/23/2024	GAW	Zoom call with client and team on development s FCC.Email correspondence with client and team of	7.5	1.50
02/26/2024	GAW	Conference with T. Franklin on preparation of leg client/case strategy.	al memo for	0,20
02/26/2024	TMF	Review Franklin Conservation Commission hearin review Franklin Wetalnds Bylaw and Regulations a WPA and Regulations concerning Freshwater Wet evaluate defense to arguments that Bylaw is more	and compare with tlands so as to	3.40
TOTAL HOUR	S AND FEES	•	10.70	\$ 5,181.00



Invoice Date: March 7, 2024 Invoice Number: 1176543

> GAW Page 4

Client: 27408

Tri-County Regional Vocational Technical High School

Matter: 001

147 Pond Street, Franklin, MA

	TIMEKEEPER SUMMARY:		
TIMEKEEPER	BILLED HOURS	BILLED RATE	BILLED AMOUNT
Glenn Wood	5.40	615.00	3,321.00
Tyler Franklin	4.00	465.00	1,860.00
Glenn Wood	1.30	0.00	0.00
TOTALS	10.70	_	\$ 5,181.00

DISBURSEMENTS:

DESCRIPTION	<u>Amount</u>
OUTSIDE MESSENGER	55.16
TOTAL DISBURSEMENTS	\$ 55.16

TOTAL AMOUNT FOR THIS INVOICE

\$ 5,236.16



Credit Card Acceptance Form

Fill out this form and fax (617) 330-7550 or email to accounting@rubinrudman.com Name (As it appears on the Card): Cardholder Address: City: _____ Province/State: ____ Postal/ZIP: ____ Credit Card Billing Address (if same enter "same"): City: _____ Province/State: _____ Postal/ZIP: _____ Home Phone Number: (_____) _____ Email Address: _____ Credit Card (Circle one) Visa Mastercard Amex Discover Client Number: _____ Matter Number: _____ Invoice Number(s): Payment Amount: Credit Card Number: EXP Date: / CCV: I authorize Rubin and Rudman LLP to make all necessary charges to my credit card account listed above. SIGNATURE _____ DATE: Billing Attorney Approval: Accounting Authorization:

BULLSEYE UNDERGROUND UTILITY LLC



25 New Chardon Street #6242 Boston, MA 02114 US +1 7819019303 oyoung@bullseyelocating.com http://www.bullseyelocating.com

INVOICE

BILL TO

Daniel B. Haynes, CPA
Tri-County Regional Vocational
Technical School District
147 Pond Street
Franklin, MA 02038

DATE	ACTIVITY	HOURS	RATW	AMOUNT
03/06/2024	Private Utility Locate Private Locate	2	200.00	400.00
	Project Title/Location: Tri-County Regional Vocational 147 Pond Street Franklin, MA 02038			
	Scope of Work: - Using (EM) Locating & and the techniques described in this proposal. Locate electrical to solar for test pits			
	*Note - Bullseye Underground Utility Locating recommends test pitting all marked facilities to confirm exact location.			
	Remember to notify your areas On Call center prior to any excavation.			
	Mobilization Fee	1	50.00	50.00

BALANCE DUE

\$450.00



Tri-County Regional Vocational Technical School SBC Meeting March 21, 2024









SBC Meeting Agenda – March 21, 2024

- Call to Order & Intro
- 2. Previous Topics & Approval of February 15, 2024, Meeting Minutes
- 3. Invoices and Commitments for approval
 - DWMP February Invoice, in the amount of \$100,000.00
 - DRA February Invoice, in the amount of \$975,000.00
 - DRA February Professional Services Invoice, in the amount of -\$8,112.50
 - Consigli February Invoice, in the amount of \$31,191.00
 - > Rubin and Rudman LLP Invoice, in the amount of \$236.16
 - Bullseve underground utility invoice, in the amount of \$450.00
 - Consigli: Sub soil exploration cost not to exceed 50k
- DRA Update
- Consigli Update
- 6. Solar Panel Array Update
- 7. Conservation Commission Update?
- 8. Other lopics not Reasonably Anticipated 48 hours prior to the Meeting
- Public Comment
- Next Meetings
- 11. Adiouri







February 15, 2024, Meeting Minutes for approval:

"Motion to appro	ve the February	15, 2024 _.
Meeting Minutes	by	, 2 nd
by		

SBC Member Vote:

- Brian Mushnick
- Karen Maguire
- Dan Haynes
- Michael Procaccini
- Jonathon Dowse
- Brendan Bowen
- Stanley Widak Jr.
- Harry Takesian
- Jane Hardin
- Bob Foley
- Lloyd "Gus" Brown

Project: Tri-County Regional Vocational Technical High School Meeting: School Building Committee Meeting No. 35 – 02/15/2024 Page: 2

Item/ No.	Description	Action
35.1	Call to order: 4:09 PM meeting was called to order by SBC Chair B. Mushnick, 9 of 11 voting members in attendance.	Record
35.2	Previous Topics & Approval of January 18,2024 Meeting Minutes: A motion to approve the January 18,2024 previous meeting minutes as submitted was made by J. Dowse and seconded by B. Foley.	Record
	Discussion: None; Roll Call Vote: B. Foley (Y), B. Bowen (Y), D. Walsh (Y), M. Procaccini (Y), K. Maguire (Y), H. Takesian (Y), J. Dowse(Y), B. Mushnick (Y); Abstentions: None. All in favor. Motion passes.	
35.3	Invoices and Commitments for approval:	Recor
	Invoice 1: DWMP January Invoice, in the amount of \$100,000,00 A motion was made by M. Procaccini and seconded by J. Dowse for the approval of the DWMP January invoice.	
	Discussion: B. Foley shares his concerns about ensuring that the payment reflects the actual progress made by the Team. He suggests a need to form a verification mechanism, for example a schedule of values.	
	T. Elmore explains that this budgeting process involves setting up different funding categories for various stages of the project. We are currently in the construction documents phase, and the invoices reflect this stage. You're making periodic monthly payments, as we go through each of these phases.	
	B. Foley comments that there is a level of uncomfortableness for me in approving these large invoices without being able to compare them to a schedule of values.	
	C. Franceschi acknowledges B. Foley's concerns about the oversight and suggests establishing a requisition subcommittee to review the architect's work and ensure progress is on track.	
	Requisition Subcommittee Members: B. Bowen, Bob Foley, Karen Maguire, Dan Haynes, Trip Elmore, Vladimir, Carl Franceschi	
	Roll Call Vote: B. Foley (Y), B. Bowen (Y), D. Walsh (Y), M. Procaccini (Y), K. Maguire (Y), H. Takesian (Y), J. Dowse(Y), D. Haynes (Y), B. Mushnick (Y); Abstentions: None. All in favor. Motion passes.	

Page 2 of 8

SBC Meeting Agenda – March 21, 2024

- Call to Order & Intro
- 2. Previous Topics & Approval of February 15, 2024. Meeting Minutes
- 3. Invoices and Commitments for approval
 - > DWMP February Invoice, in the amount of \$100,000.00
 - > DRA February Invoice, in the amount of \$975,000.00
 - > DRA February Professional Services Invoice, in the amount of -\$8,112.50
 - Consigli February Invoice, in the amount of \$31,191.00
 - > Rubin and Rudman LLP Invoice, in the amount of \$236.16
 - > Bullseye underground utility invoice, in the amount of \$450.00
 - > Consigli: Sub soil exploration cost not to exceed 50K
- DRA Update
- 5. Consigli Update
- 6. Solar Panel Array Update
- Conservation Commission Update
- 8. Other Topics not Reasonably Anticipated 48 hours prior to the Meeting
- Public Comment
- 10. Next Meetings
- 11. Adjour







Budget Update



March 19, 2024

Project Name: Tri-County

Subject: Budget Update

1. Invoice(s): recommended for payment

Vendor	Invoice	Amount		
Dore + Whittier	25	\$100,000.00		
DRA	23	\$975,000.00		
DRA	PSS6-2	(\$8,112.50)		
CCC	3	\$31,191.00		
Rubin & Rodman	1176543	\$236.16		
Bullseye	201655	\$450.00		

\$1,098,765

- 2. New Commitment(s):
- 3. Budget Revision Request(s): -

4. MSBA Reimbursement Status:

PR No.	Payment Request Date	Submitted Amount	Ineligible Project Costs	Eligible Project Costs	Eligible Grant	Recommended Payment Amount	MSBA Last Payment Date	MSBA Payment Amount
1	12/6/2023	\$10,000	\$0	\$10,000	\$5,289	\$0	1/28/2022	\$5,289
2	2/17/2022	\$20,000	\$0	\$20,000	\$10,578	\$0	3/31/2022	\$10,578
3	4/8/2022	\$39,250	\$0	\$39,250	\$20,759	\$0	5/19/2022	\$20,759
4	6/23/2022	\$102,000	\$0	\$102,000	\$53,948	\$0	7/28/2022	\$53,948
5	8/1/2022	\$49,880	\$0	\$49,880	\$26,382	\$0	9/9/2022	\$26,382
6	10/26/2022	\$67,750	\$0	\$67,750	\$35,833	\$0	12/15/2022	\$35,833
7	12/20/2022	\$98,886	\$0	\$98,886	\$52,301	\$0	2/2/2023	\$52,300
8	3/10/2022	\$117,740	\$0	\$117,740	\$62,273	\$0	4/6/2023	\$62,273
9	5/16/2023	\$145,750	\$0	\$145,750	\$77,087	\$0	6/23/2023	\$77,087
10	8/14/2023	\$311,790	\$0	\$311,790	\$164,906	\$0	9/8/2023	\$158,006
11	12/14/2023	\$34,695	\$0	\$34,695	\$54,967	\$61,867		\$0
12	2/14/2024	\$1,575,000	\$0	\$1,575,000	\$890,820	\$952,687		\$0
Total		\$2,572,741	\$0	\$2,572,741	\$1,455,143			\$502,455

DWMP February Invoice

Motion to approve the DWMP February	
Invoice, in the amount of \$100,000.00	
by, 2 nd by	

SBC Member Vote:

- Brian Mushnick
- Karen Maguire
- Dana Walsh
- Dan Haynes
- Michael Procaccini
- Jonathon Dowse
- Brendan Bowen
- Stanley Widak Jr.
- Harry Takesian
- Jane Hardin
- Bob Foley
- Lloyd "Gus" Brown

Dore and Whittier Management Partners, LLC

Please send payments to; 212 Battery Street Suite 1 Burlington, VT 05401

Tri-County Regional Technical School District

147 Pond Street Franklin, MA 02038 Invoice number 00025
Date 02/27/2024

Project 21-0122 TRI-COUNTY REGIONAL TECHNICAL HIGH SCHOOL

Description		Contract Amount	Prior Billed	Current Billed	Remaining	Total Billed
Pre Designer Selection		40,000.00	40,000.00	0.00	0.00	40,000.00
Feasibility Phase		130,000.00	130,000.00	0.00	0.00	130,000.00
Schematic Design		105,000.00	105,000.00	0.00	0.00	105,000.00
Construction Documents		1,900,000.00	400,000.00	100,000.00	1,400,000.00	500,000.00
Bidding		200,000.00	0.00	0.00	200,000.00	0.00
Construction Administration		4,700,000.00	0.00	0.00	4,700,000.00	0.00
Closeout		200,000.00	0.00	0.00	200,000.00	0.00
	Total	7.275.000.00	675,000.00	100,000.00	6,500,000.00	775.000.00

Invoice total 100,000.00

Aging Summary

Invoice Number	Invoice Date	Outstanding	Current	Over 30	Over 60	Over 90	Over 120
00024	01/30/2024	100,000.00	100,000.00				
00025	02/27/2024	100,000.00	100,000.00				
	Total	200,000.00	200,000.00	0.00	0.00	0.00	0.00

DRA February Invoice

Motion to a	approve the DRA February	
nvoice, in t	he amount of <u>\$975,000.00</u>	
оу	, 2 nd by	•

SBC Member Vote:

- Brian Mushnick
- Karen Maguire
- Dana Walsh
- Dan Haynes
- Michael Procaccini
- Jonathon Dowse
- Brendan Bowen
- Stanley Widak Jr.
- Harry Takesian
- Jane Hardin
- Bob Foley
- Lloyd "Gus" Brown



Drummey Rosane Anderson, Inc.

Planning | Architecture | Interior Design

Invoice

Karen Maguire Superintendent Tri-County Regional Vocational Technical School Di 147 Pond Street Franklin, MA 02038 February 29, 2024 Project No: 22001.00 Invoice No: 0000023

Total this Invoice

\$975,000.00

Project-Tri-County Regional Vocational Technical

Professional Services from February 1, 2024 to February 29, 2024

Billing Phase	Fee	Percent Complete	Earned	
Feasibility Study	285,000.00	100.00	285,000.00	
Schematic Design	340,000.00	100.00	340,000.00	
Design Development	7,500,000.00	43.00	3,225,000.00	
Construction Documents	9,550,000.00	0.00	0.00	
Bidding	150,000.00	0.00	0.00	
Construction	3,800,000.00	0.00	0.00	
Completion	150,000.00	0.00	0.00	
Total Fee	21,775,000.00		3,850,000.00	
		Previous Fee Billing	2,875,000.00	
		Current Fee Billing	975,000.00	
	Total Fee			975,000.00

If you have any questions regarding this invoice, please contact Judy Gill at 617-964-1700 or e-mail gill@ draws.com.

DRA February Professional Services Invoice

Motion to approve the DRA Febru	ary Professiona
Services Invoice, in the amount of	- <u>\$8,112.50</u> by
, 2 nd by	

SBC Member Vote:

- Brian Mushnick
- Karen Maguire
- Dana Walsh
- Dan Haynes
- Michael Procaccini
- Jonathon Dowse
- Brendan Bowen
- Stanley Widak Jr.
- Harry Takesian
- Jane Hardin
- Bob Foley
- Lloyd "Gus" Brown



Drummey Rosane Anderson, Inc.

Planning | Architecture | Interior Design

Invoice

Franklin, MA 02038

Karen Maguire February 29, 2024
Superintendent Project No: 22001.06
Tri-County Regional Vocational Technical School Di Invoice No: 0000002
147 Pond Street

Project-Tri-County Regional Amendment 6 Geotech

Professional Services from February 1, 2024 to February 29, 2024

Consultants

 O'Reilly, Talbot & Okun Associates, Inc. /lnv 55025 -Note 1
 -12,000.00

 O'Reilly, Talbot & Okun Associates, Inc. /lnv 55116-Note 2
 - 1,000.00

 O'Reilly, Talbot & Okun Associates, Inc. /lnv 55147
 5,625.00

 Total Consultants
 1.1 times

Billing Limits	Current	Prior	To-Date
Total Billings	-8,112.50	33,672.10	25,559.60
Limit			123,200.00
Remaining			97,640.40

Total this Invoice -\$8,112.50

-8,112.50

Note 1) This was invoiced in January in error. These tasks are Preliminary Services and are DRA's responsibility.

Note 2) This was invoiced in January in error. This task of Design Phase Meetings is DRA's responsibility.

Consigli February Invoice

Motion to app	rove the Consigli .	January Invoice, ir
the amount of	\$31,191.00	
by	, 2 nd by	<i>"</i>

SBC Member Vote:

- Brian Mushnick
- Karen Maguire
- Dana Walsh
- Dan Haynes
- Michael Procaccini
- Jonathon Dowse
- Brendan Bowen
- Stanley Widak Jr.
- Harry Takesian
- Jane Hardin
- Bob Foley
- Lloyd "Gus" Brown



Consigli Construction Co., Inc. 72 Sumner Street Milford, MA 01757 (508)473-2580

Tri County Reg. Voc. Technical HS 147 Pond Street Franklin, MA 02038

INVOICE ID: 3 DATE: February 29,2024

Period From: 2/2/2024 To: 2/29/2024

Item Id	Description	Contract Amount	Percent Complete	Total Billed	Previous Billed	Total This Invoice
	Tri County Reg. Voc. Tech. HS PO 20231640					
	Schematic Estimate Requirement	25,000.00	100.00 %	25,000.00	25,000.00	
22-200	Post-SD Precon Services	374,300.00	16.67 %	62,382.00	31,191.00	31,191.00
	Total	399,300.00	21.88 %	87,382.00	56,191.00	31,191.00
Contract Sur	mmany					
	contract amount	39	99,300.00			
	ed changes		0.00			
	contract amount		99,300.00			
	d to date		37.382.00			
Remain	ing to invoice	3	11,918.00			
Current	Payment Due	\$3	31,191.00			
Percent	billed		21.88 %			
Retaina	ge balance		0.00			
Approved by	r.					
Name:						
Title:						
Date:						

Rubin and Rudman LLP Invoice

Motion t	to approve the Rubin and Rudman	LLI
nvoice, i	in the amount of <u>\$236.16</u>	
оу	, 2 nd by	<i>.</i> "

SBC Member Vote:

- Brian Mushnick
- Karen Maguire
- Dana Walsh
- Dan Haynes
- Michael Procaccini
- Jonathon Dowse
- Brendan Bowen
- Stanley Widak Jr.
- Harry Takesian
- Jane Hardin
- Bob Foley
- Lloyd "Gus" Brown



53 State Street Boston, MA 02109 7 617-330-7000 F 617-330-7550

Tri-County Regional Vocational Technical High School Karen Maguire 147 Pond Street Franklin, MA 02038

> Invoice Date: March 7, 2024 Invoice Number: 1176543

voice Number: 117654:

TOTAL AMOUNT DUE THIS INVOICE \$ 236.16

Client: 27408 Matter: 001	Tri-County Regional Vocational Technical High School 147 Pond Street, Franklin, MA		
TOTAL FEES THIS INVOICE	re .	5.181.00	
TOTAL DISBURSEMENTS THIS INVOICE		55.16	
		55120	
TOTAL AMOUNT THIS I	NVOICE	\$ 5,236.16 (5,000.00	
Less Trust Applied	Less Trust Applied		
TOTAL AMOUNT DUE		\$ 236.16	
TOTAL AMOUNT DOL		7 230.20	
	Please Lise One of our Convenient Payment Ontions		
Payment via ACH:	Please Use One of our Convenient Payment Options Bank Name: Eastern Bank		
Payment via ACH:			
Payment via ACH:	Bank Name: Eastern Bank		
Payment via ACH:	Bank Name: Eastern Bank ABA/Routing Number: 011301798		
	Bank Name: Eastern Bank ABA/Routing Number: 011301798 Account Number: 601621569 Bank Name: Eastern Bank		
Payment via Wire:	Bank Name: Eastern Bank ABA/Routing Number: 011301798 Account Number: 601621569 Bank Name: Eastern Bank		
Payment via Wire:	Bank Name: Eastern Bank ABA/Routing Number: 011301798 Account Number: 601621569 Bank Name: Eastern Bank ABA/Routing Number: 011301798		
Payment via Wire:	Bank Name: Eastern Bank ABA/Routing Number: 011301798 Account Number: 601621569 Bank Name: Eastern Bank ABA/Routing Number: 011301798 SWIFT Code: EASRUS3B		
Payment via Wire:	Bank Name: Eastern Bank ABA/Routing Number: 011301798 Account Number: 601621569 Bank Name: Eastern Bank ABA/Routing Number: 011301798 SWIFT Code: EASRUS3B Account Number: 601621569		
Payment via Wire: (bank wire fees may apply)	Bank Name: Eastern Bank ABA/Routing Number: 011301798 Account Number: 601621569 Bank Name: Eastern Bank ABA/Routing Number: 011301798 SWIFT Code: EASRUS3B Account Number: 601621569 Bank Address: 195 Market Street, Lynn MA 01901		
Payment via Wire: (bank wire fees may apply)	Bank Name: Eastern Bank ABA/Routing Number: 011301798 Account Number: 601621569 Bank Name: Eastern Bank ABA/Routing Number: 011301798 SWIFT Code: EASRUS38 Account Number: 601621569 Bank Address: 195 Market Street, Lynn MA 01901 Rubin and Rudman LLP 53 State Street 15th Floor		
Payment via Wire: (bank wire fees may apply)	Bank Name: Eastern Bank ABA/Routing Number: 011301798 Account Number: 601621569 Bank Name: Eastern Bank ABA/Routing Number: 011301798 SWIFT Code: EASRUS3B Account Number: 601621569 Bank Address: 195 Market Street, Lynn MA 01901 Rubin and Rudman LLP 53 State Street		

Bullseye Underground Utility LLC Invoice

Motion to app	prove the Bullseye	Underground
Jtility LLC, Inv	oice, in the amour	nt of \$450.00
).)	, 2 nd bv	"
ру		·

SBC Member Vote:

- Brian Mushnick
- Karen Maguire
- Dana Walsh
- Dan Haynes
- Michael Procaccini
- Jonathon Dowse
- Brendan Bowen
- Stanley Widak Jr.
- Harry Takesian
- Jane Hardin
- Bob Foley
- Lloyd "Gus" Brown

BULLSEYE UNDERGROUND UTILITY LLC



25 New Chardon Street #6242 Boston, MA 02114 US +1 7819019303 oyoung@bullseyelocating.com http://www.bullseyelocating.com

INVOICE

BILL TO

Daniel B. Haynes, CPA Tri-County Regional Vocational Technical School District 147 Pond Street Franklin, MA 02038

DATE	ACTIVITY	HOURS	RATW	AMOUNT
03/06/2024	Private Utility Locate Private Locate	2	200.00	400.00
	Project Title/Location: Tri-County Regional Vocational 147 Pond Street Franklin, MA 02038			
	Scope of Work: - Using (EM) Locating & and the techniques described in this proposal. Locate electrical to solar for test pits			
	*Note - Bullseye Underground Utility Locating recommends test pitting all marked facilities to confirm exact location.			
	Remember to notify your areas On Call center prior to any excavation.			
	Mobilization Fee	1	50.00	50.00


BALANCE DUE

\$450.00



Legend:

Green Dots = Test Pits Red Dots = Borings

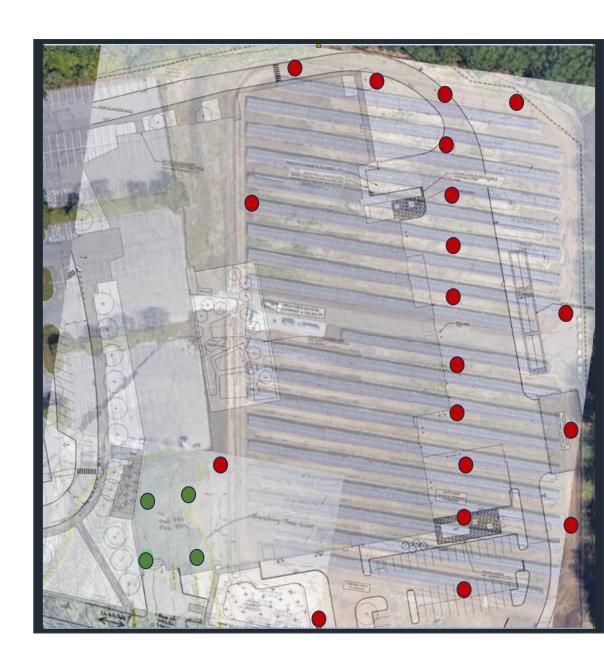

SBC Meeting Agenda – March 21, 2024

- 1. Call to Order & Intro
- 2. Previous Topics & Approval of February 15, 2024, Meeting Minute
- 3. Invoices and Commitments for approval
 - DWMP February Invoice, in the amount of \$100,000.00
 - DRA February Invoice, in the amount of \$975,000.00
 - DRA February Professional Services Invoice, in the amount of -\$8.112.50
 - > Consigli February Invoice, in the amount of \$31.191.00
 - Rubin and Rudman LLP Invoice, in the amount of \$236.16
 - Bullseye underground utility invoice, in the amount of \$450.00
 - Consigli: Sub soil exploration cost not to exceed 50l

4. DRA Update

- 5. Consigli Update
- Consigli: Sub soil exploration cost not to exceed 70k
- 7. Solar Panel Array Update
- 8. Conservation Commission Update?
- Other Topics not Reasonably Anticipated 48 hours prior to the Meeting
- 10 Public Comment
- 11. Next Meetings
- 12. Adjouri






























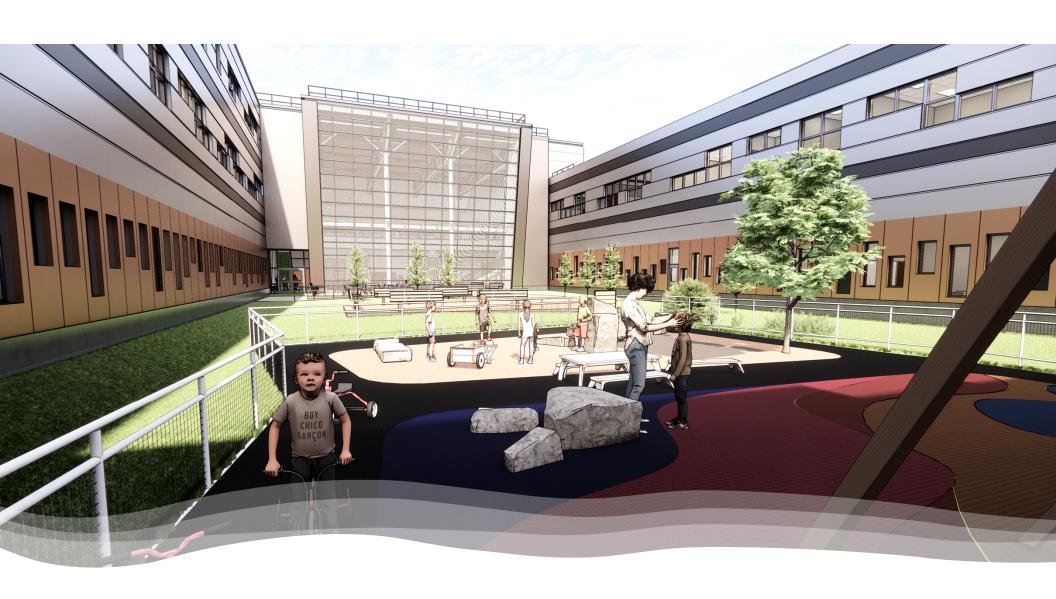

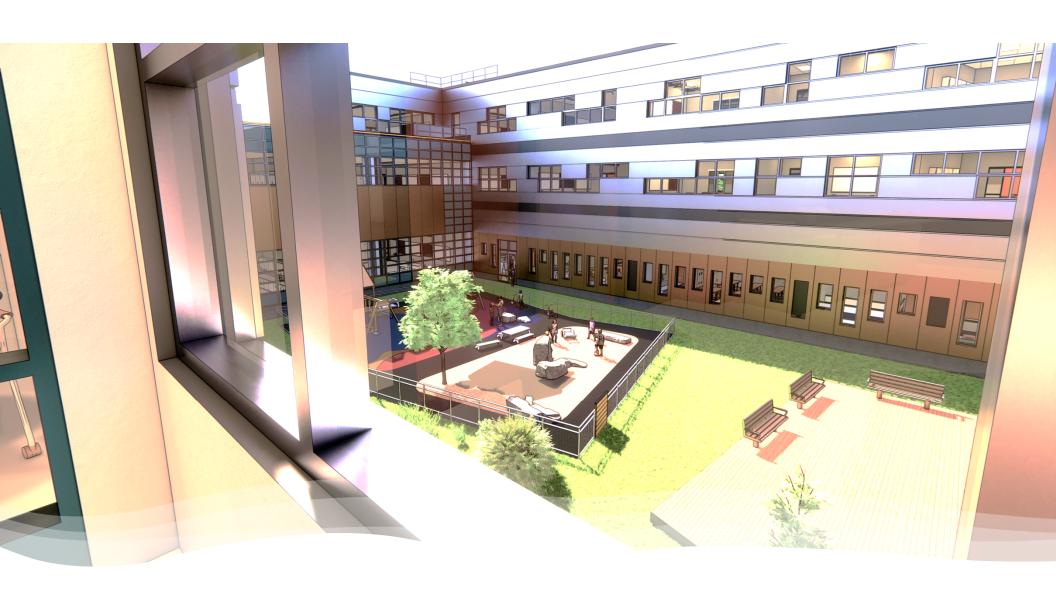

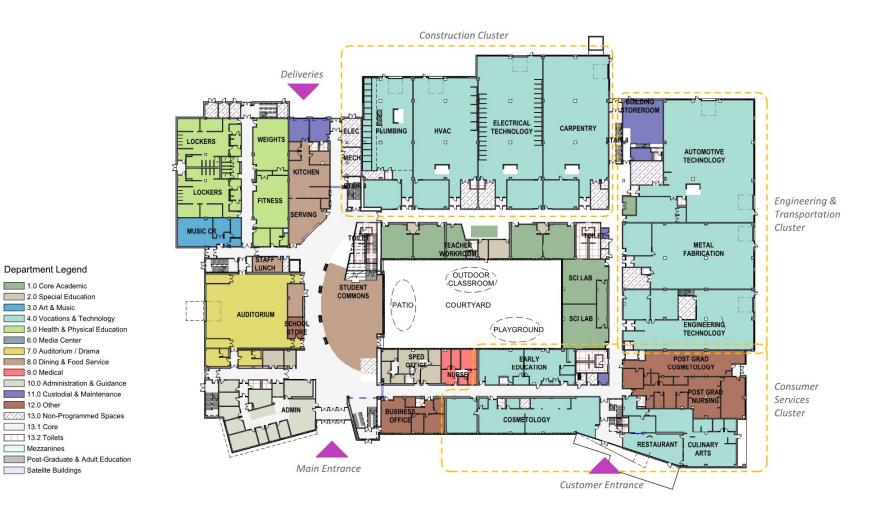

Department Legend

1.0 Core Academic

2.0 Special Education

4.0 Vocations & Technology

8.0 Dining & Food Service 9.0 Medical

11.0 Custodial & Maintenance

13.0 Non-Programmed Spaces

3.0 Art & Music


6.0 Media Center 7.0 Auditorium / Drama

12.0 Other

13.1 Core 13.2 Toilets

Mezzanines

Satelite Buildings

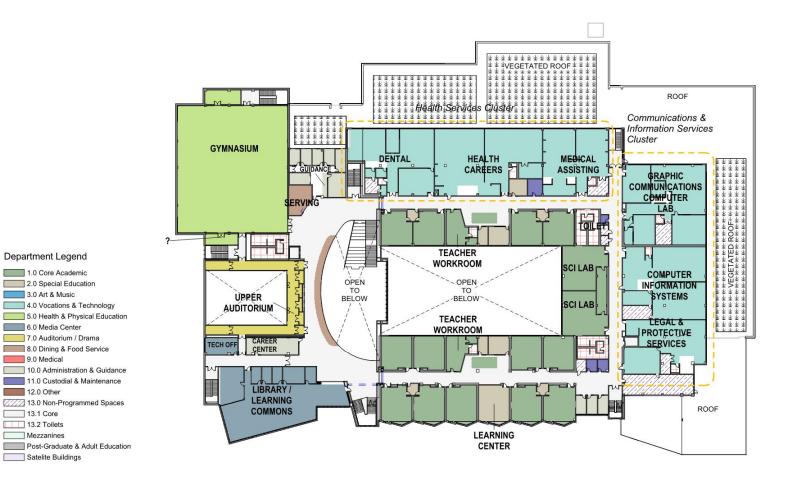

Department Legend

1.0 Core Academic

2.0 Special Education

3.0 Art & Music

6.0 Media Center

9.0 Medical

12.0 Other


13.1 Core 13.2 Toilets

Mezzanines

Satelite Buildings

7.0 Auditorium / Drama

8.0 Dining & Food Service

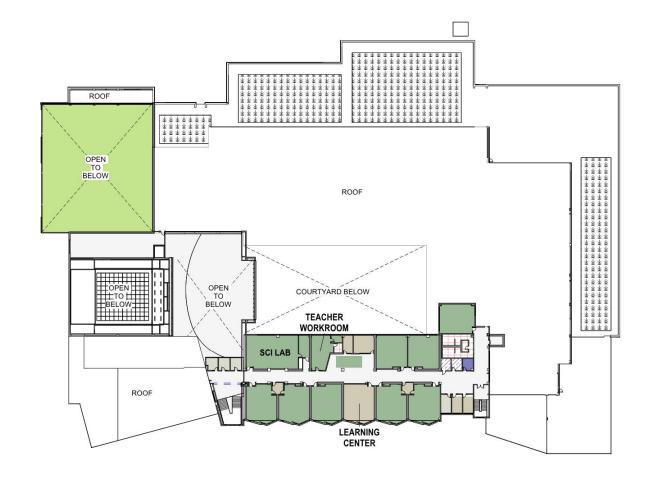

Department Legend

1.0 Core Academic
2.0 Special Education
3.0 Art & Music
4.0 Vocations & Technology
5.0 Health & Physical Education
6.0 Media Center

7.0 Auditorium / Drama 8.0 Dining & Food Service 9.0 Medical

10.0 Administration & Guidance
11.0 Custodial & Maintenance
12.0 Other

13.0 Non-Programmed Spaces
13.1 Core

13.2 Toilets
Mezzanines


Post-Graduate & Adult Education

Satelite Buildings







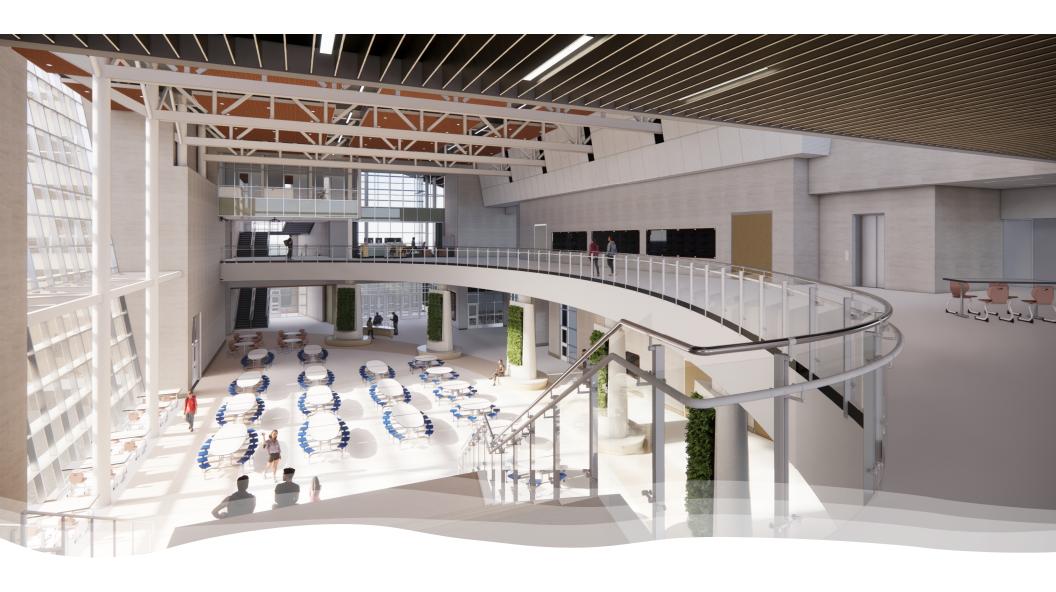
















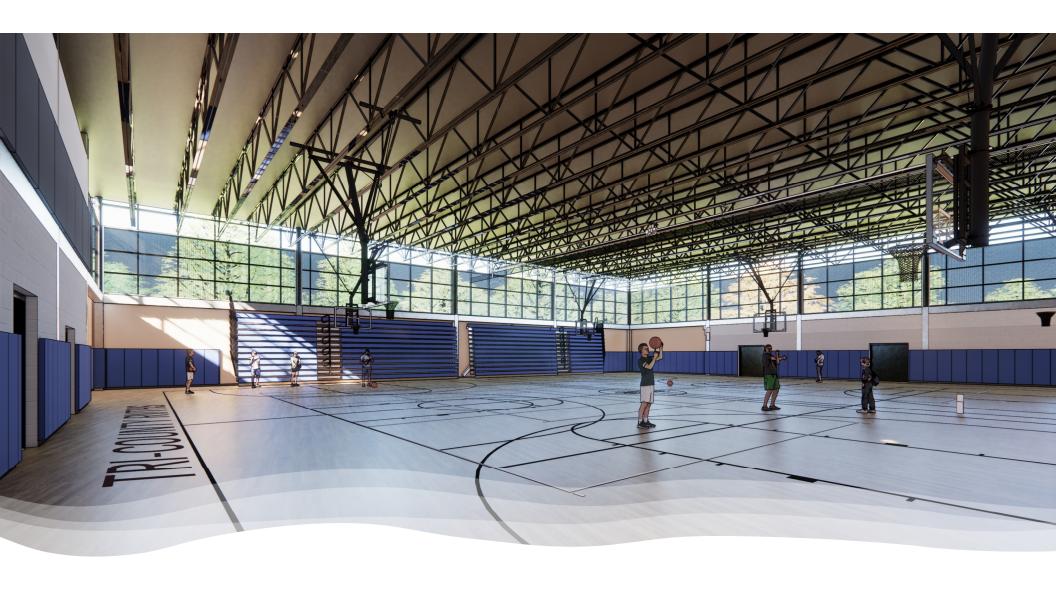














Alternate with Terrazzo Floor at Student Commons



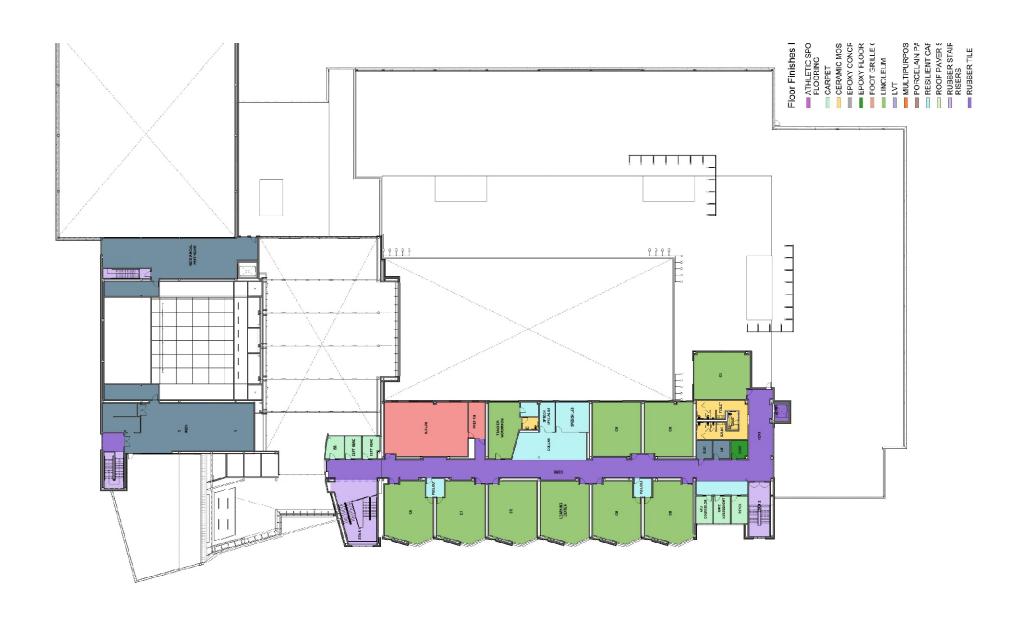

•Questions?



SBC Meeting Agenda – March 21, 2024

- Call to Order & Intro
- 2. Previous Topics & Approval of February 15, 2024. Meeting Minutes
- 3. Invoices and Commitments for approval
 - ▶ DWMP February Invoice, in the amount of \$100,000.00
 - DRA February Invoice, in the amount of \$975,000.00
 - DRA February Professional Services Invoice, in the amount of -\$8,112.50
 - Consigli February Invoice, in the amount of \$31,191.00
 - Rubin and Rudman LLP Invoice, in the amount of \$236.16
 - ➤ Bullseve underground utility invoice, in the amount of \$450.00
 - Consigli: Sub soil exploration cost not to exceed 50k
- DRA Undate


5. Consigli Update


- 6. Solar Panel Array Update
- Conservation Commission Update:
- 8. Other Topics not Reasonably Anticipated 48 hours prior to the Meeting
- Public Comment
- 10. Next Meeting:
- 11. Adjourn







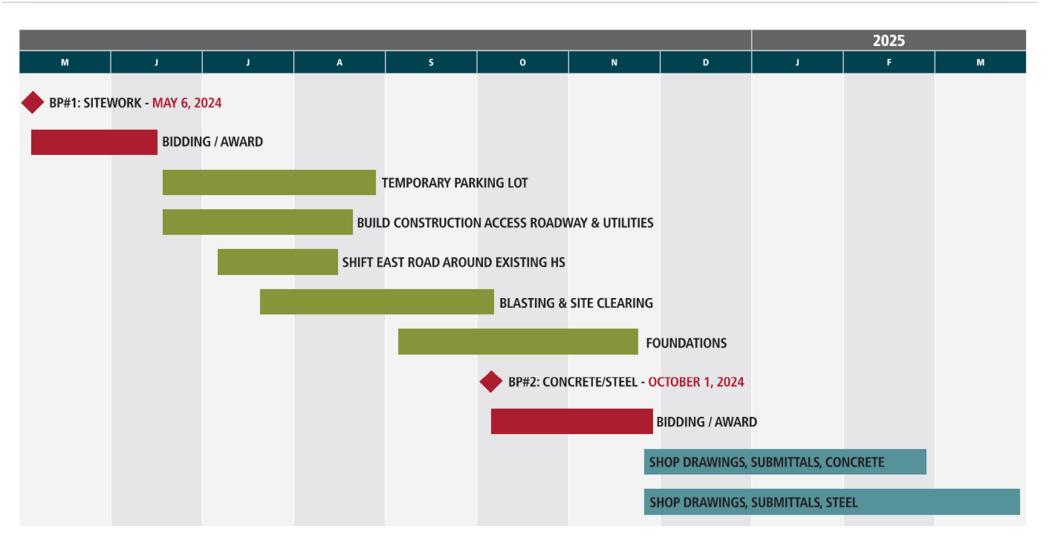

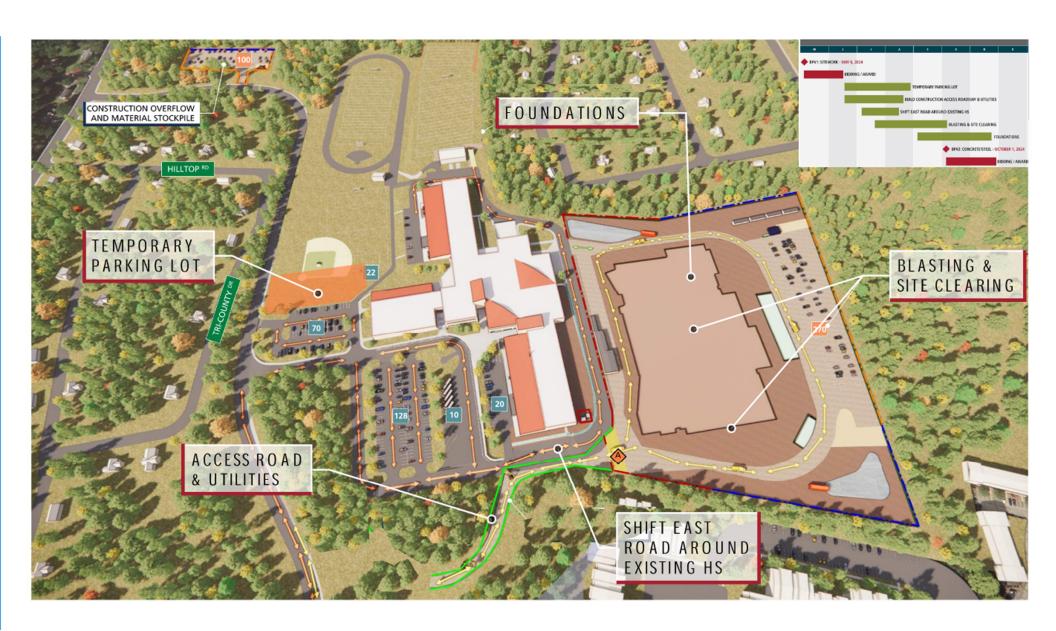

- Call to Order & Intro
- 2. Previous Topics & Approval of February 15, 2024, Meeting Minutes
- 3. Invoices and Commitments for approval
 - ▶ DWMP February Invoice, in the amount of \$100,000.00
 - DRA February Invoice, in the amount of \$975,000.00
 - DRA February Professional Services Invoice, in the amount of -\$8,112.50
 - Consigli February Invoice, in the amount of \$31,191.00
 - ➤ Rubin and Rudman LLP Invoice, in the amount of \$236.16
 - ➤ Bullseve underground utility invoice, in the amount of \$450.00
 - Consigli: Sub soil exploration cost not to exceed 50k
- DRA Undate
- Consigli Update


6. Solar Panel Array Update

- Conservation Commission Update:
- 8. Other Topics not Reasonably Anticipated 48 hours prior to the Meeting
- Public Comment
- 10. Next Meeting:
- 11. Adjourn










Early termination column 1

Early Termination Occurs in Year 9: Column 1 Early Termination Fee where Purchaser does not take Title to the System (\$/Wdc including costs of removal).

Year 9 Calculation:

1,306,800 X 2.23 = \$2,914,164





Early Termination Column 2

Early Termination Fee where Purchaser takes Title to the System (\$/Wdc, does not include costs of removal)

Purchase Date Occurs on the 91st day following: (Each "Anniversary" shall refer to the anniversary of the Commercial Operation Date of 5/22/2015)

Year 8 Anniversary Calculation:

1,306,800 X 1.73 = \$2,260,764

Year 9 Anniversary Calculation:

1,306,800 X 1.66 = \$2,169,288

Cost comparison Early termination

Column 1 Cost \$2,914,164 Column 2 Cost \$2,260,764

Cost Difference \$653,400

Solect Energy quote to dispose of solar array.

?



Other Factors

- Timing
- Procurement of solar array removal
- Continue to work with Luminace

- Call to Order & Intro
- 2. Previous Topics & Approval of February 15, 2024, Meeting Minutes
- 3. Invoices and Commitments for approval
 - DWMP February Invoice, in the amount of \$100,000.00
 - > DRA February Invoice, in the amount of \$975,000.00
 - DRA February Professional Services Invoice, in the amount of -\$8,112.50
 - Consigli February Invoice, in the amount of \$31,191.00
 - > Rubin and Rudman LLP Invoice, in the amount of \$236.16
 - Bullseye underground utility invoice, in the amount of \$450.00
 - Consigli: Sub soil exploration cost not to exceed 50K
- DRA Update
- Consigli Update
- 6. Solar Panel Array Update

7. Conservation Commission Update

- 8. Other Topics not Reasonably Anticipated 48 hours prior to the Meeting
- Public Comment
- 10. Next Meetings
- 11. Adjour









- Call to Order & Intro
- 2. Previous Topics & Approval of February 15, 2024, Meeting Minutes
- 3. Invoices and Commitments for approval
 - DWMP February Invoice, in the amount of \$100,000.00
 - DRA February Invoice, in the amount of \$975,000.00
 - DRA February Professional Services Invoice, in the amount of -\$8,112.50
 - Consigli February Invoice, in the amount of \$31,191.00
 - Rubin and Rudman LLP Invoice, in the amount of \$236.16
 - Bullseye underground utility invoice, in the amount of \$450.00
 - Consigli: Sub soil exploration cost not to exceed 50k
- DRA Update
- 5. Consigli Update
- 6. Solar Panel Array Update
- 7. Conservation Commission Update
- 8. Other Topics not Reasonably Anticipated 48 hours prior to the Meeting
- 9. Public Comment
- 10. Next Meetings
- 11. Adiouri







Next Meetings

SBC MEETING NO.037

APRIL 25, 2024- DD APPROVAL



- Call to Order & Intro
- 2. Previous Topics & Approval of February 15, 2024. Meeting Minutes
- 3. Invoices and Commitments for approval
 - DWMP February Invoice, in the amount of \$100,000.00
 - DRA February Invoice, in the amount of \$975,000.00
 - DRA February Professional Services Invoice, in the amount of -\$8,112.50
 - Consigli February Invoice, in the amount of \$31,191.00
 - > Rubin and Rudman LLP Invoice, in the amount of \$236.16
 - ➤ Bullseve underground utility invoice, in the amount of \$450.00
 - Consigli: Sub soil exploration cost not to exceed 50k
- DRA Update
- Consigli Update
- 6. Solar Panel Array Update
- 7. Conservation Commission Update:
- 8. Other Topics not Reasonably Anticipated 48 hours prior to the Meeting
- 9 Public Comment
- Next Meetings

11. Adjourn







Adjourn: Motion to Adjourn by _______, 2nd by

SBC Member Vote:

- Brian Mushnick
- Karen Maguire
- Dana Walsh
- Dan Haynes
- Michael Procaccini
- Jonathon Dowse
- Brendan Bowen
- Stanley Widak Jr.
- Harry Takesian
- Jane Hardin
- Bob Foley
- Lloyd "Gus" Brown









